

Construction Update

Devonport Town Centre | Safety Improvements

On behalf of everyone at Auckland Transport we hope this newsletter finds you and your whānau well.

Here's a quick update from the project team about the work that is happening in and around Devonport.

The construction of the Devonport Town Centre Safety Improvement project started on 12 June 2023 after our consultation and significant community input. We acknowledge everyone who shared their views with AT including representatives from the community, Business Association, Bike Auckland, Devonport-Takapuna Local Board and Ward Councillors.

We would like to thank you for your patience while this important safety work is carried out. To minimise disruption, the works will be carried out in stages. Construction phases location and timeline can be found on page 2.

For regular updates, please visit our website:

[AT.govt.nz/devonportsafespeeds](https://at.govt.nz/devonportsafespeeds)

or scan the QR code.




Construction of the Calliope Road raised pedestrian crossing



What we are doing

We will be building raised crossings, a separated cycleway, upgrading streetlighting at pedestrian crossings, minor footpath upgrades, and making other safety improvements around the area.

These improvements will slow down traffic to create an environment that is safer for everyone. Check out our staging map below that shows how we will be constructing our safety improvements.

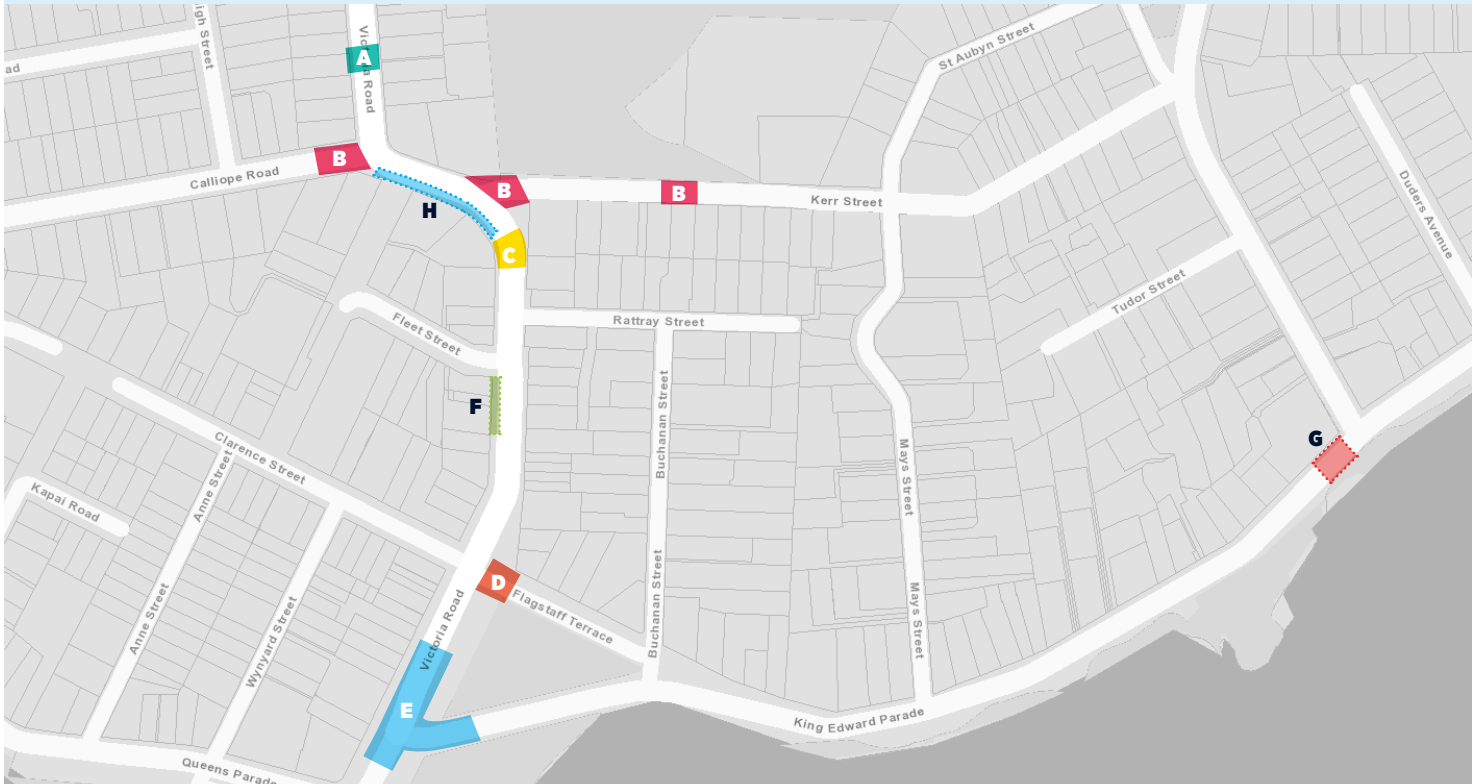

Construction Phase Map

Safety Improvementents

Timeline 2023*

Construction Phases		JUN	JUL	AUG	SEP	OCT
A	Upgrade to raised crossing	✓				
B	New raised crossings		✓			
C	Pedestrian crossing improvements					
D	New raised crossing					
E	Upgrade to two existing crossings and one new raised crossing					
F	Upgrade bus stop					
G	New zebra crossing	✓				
H	New cycleway					

*Subject to weather condition and please refer to the works notification letter for more details.



What we've been up to

Calliope Road and Kerr Street raised crossings

Despite the challenging weather, we successfully completed two raised crossings on Kerr Street during the school holidays. Calliope Road was subsequently finished and both are well used by the public.



Phase B Kerr Street and Calliope Road raised crossings





Meet our team


With nine years' experience in the construction industry, Epa was hired as a specialist operator and has worked his way to the foreman position within four years at Fulton Hogan.

Epa has been the main driving force behind the construction operations, working alongside the ground staff as well as office staff to hit target milestones.

Epa's highlight on this project so far is delivering two speed tables and pouring a third within the space of two weeks during the recent school holidays.

As a family man, his motivation for the energy and effort in his work comes from his family and improving the network to create a safe environment for his children.


In his spare time, Epa plays touch rugby, as well as spend time with his family and friends.

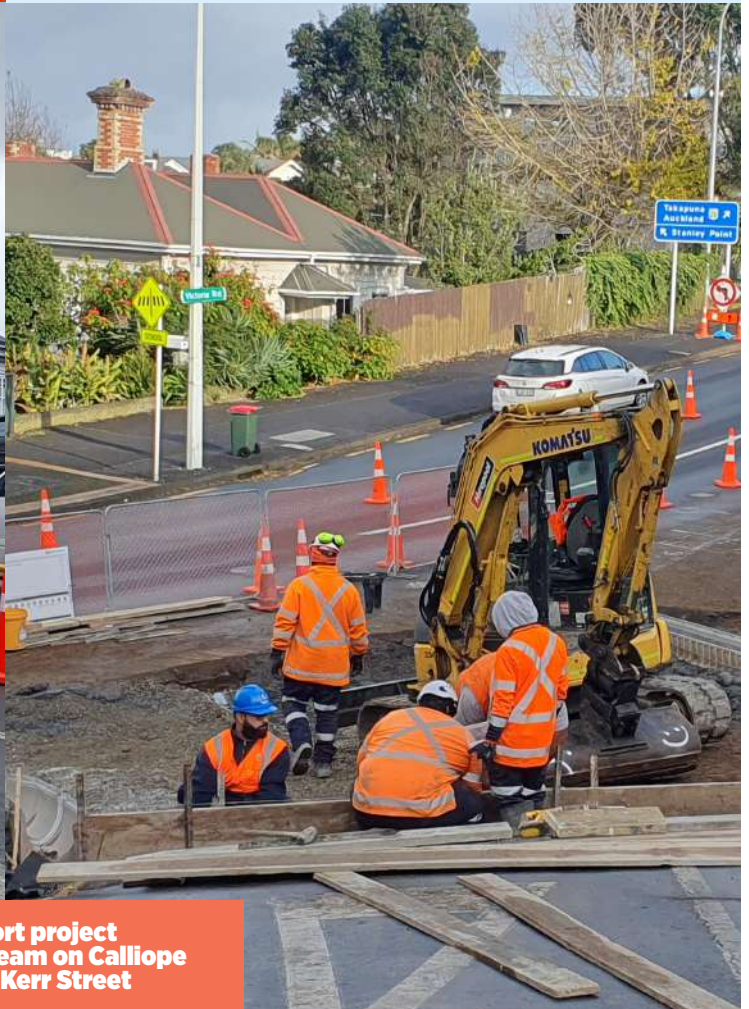

Devonport project construction team on Calliope Road and Kerr Street



Devonport locals using the Kerr Street crossing

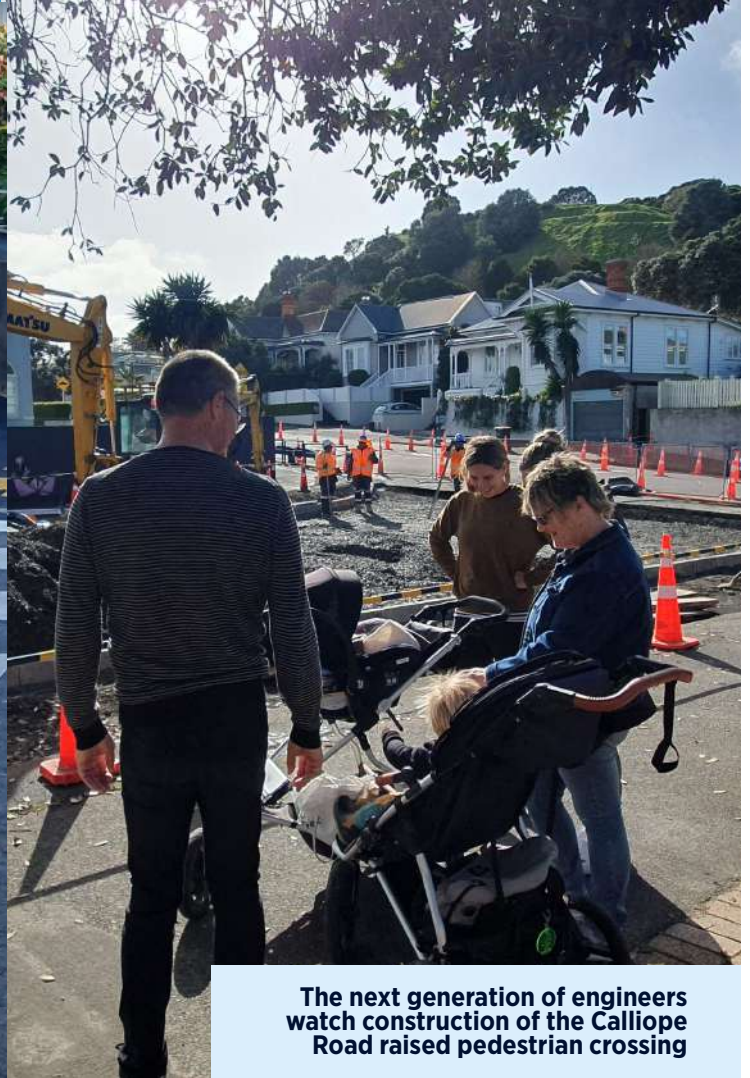

The next generation of engineers watch construction of the Calliope Road raised pedestrian crossing



Treats from our kind-hearted neighbours



Thank you for your order
0800 147 433

ATTN: Eiran 097 615 4581

Thank you for your order
0800 147 433

CM GROUP



Next up
(weather dependant)

In August, we will complete Phase D, F and G of the project


Phase D consists of a raised pedestrian crossing on Flagstaff Terrace

Phase F consists of the bus stop upgrade on Victoria Road

Phase G consists of the zebra crossing on King Edward Parade (adjacent to Church Street)



Phase F Bus stop upgrade

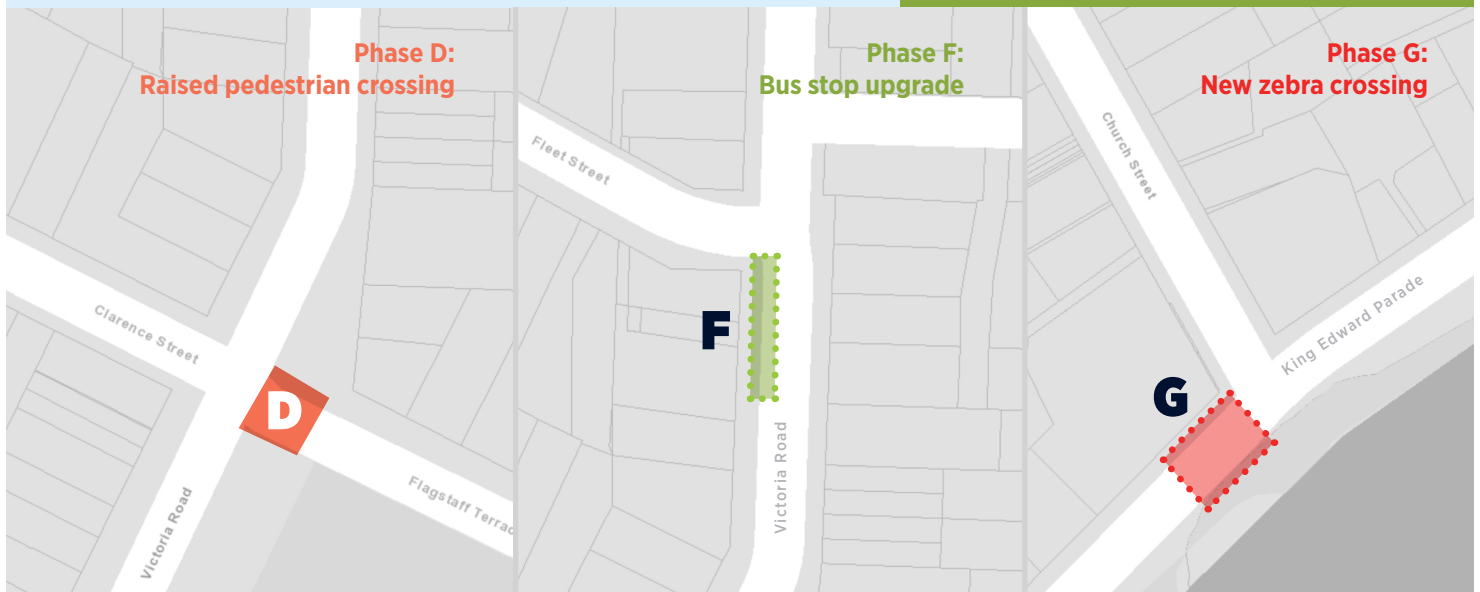

For your safety

Traffic management is in place to keep the public and our crew safe while we carry out this work. Please make sure children and dogs in your care do not enter any fenced areas and be aware of the trucks and other machinery in the area.

Pedestrians and cyclists are being diverted around our sites. Please follow our detour routes and stay safe. If you would like further information regarding the project, please contact us using the details provided at the end of this newsletter.

We have a weekly drop-in session at the Devonport Library, where you can get up to date information about the project

Auckland Transport and Fulton Hogan project staff will be available on Thursday's, from 10 am to 11 am, to answer your questions and queries.



For questions about construction activities (machinery, traffic management etc.) contact Fulton Hogan Stakeholder Manager, Emma Cushnie on **027 532 4305** or email Emma.Cushnie@fultonhogan.com
For project related questions, please contact AT on **09 355 3553** or email projects@AT.govt.nz

